CityNexus | System at a glance

Four layers and one rule: the agent proposes, the domain services decide. Every box is a real component in the reviewed tree.

CNX-SE-DECK-1 architecture • plan sha256 4cd35d0725c2 • generated 2026-10-23 02:17
generated 2026-10-23 02:17

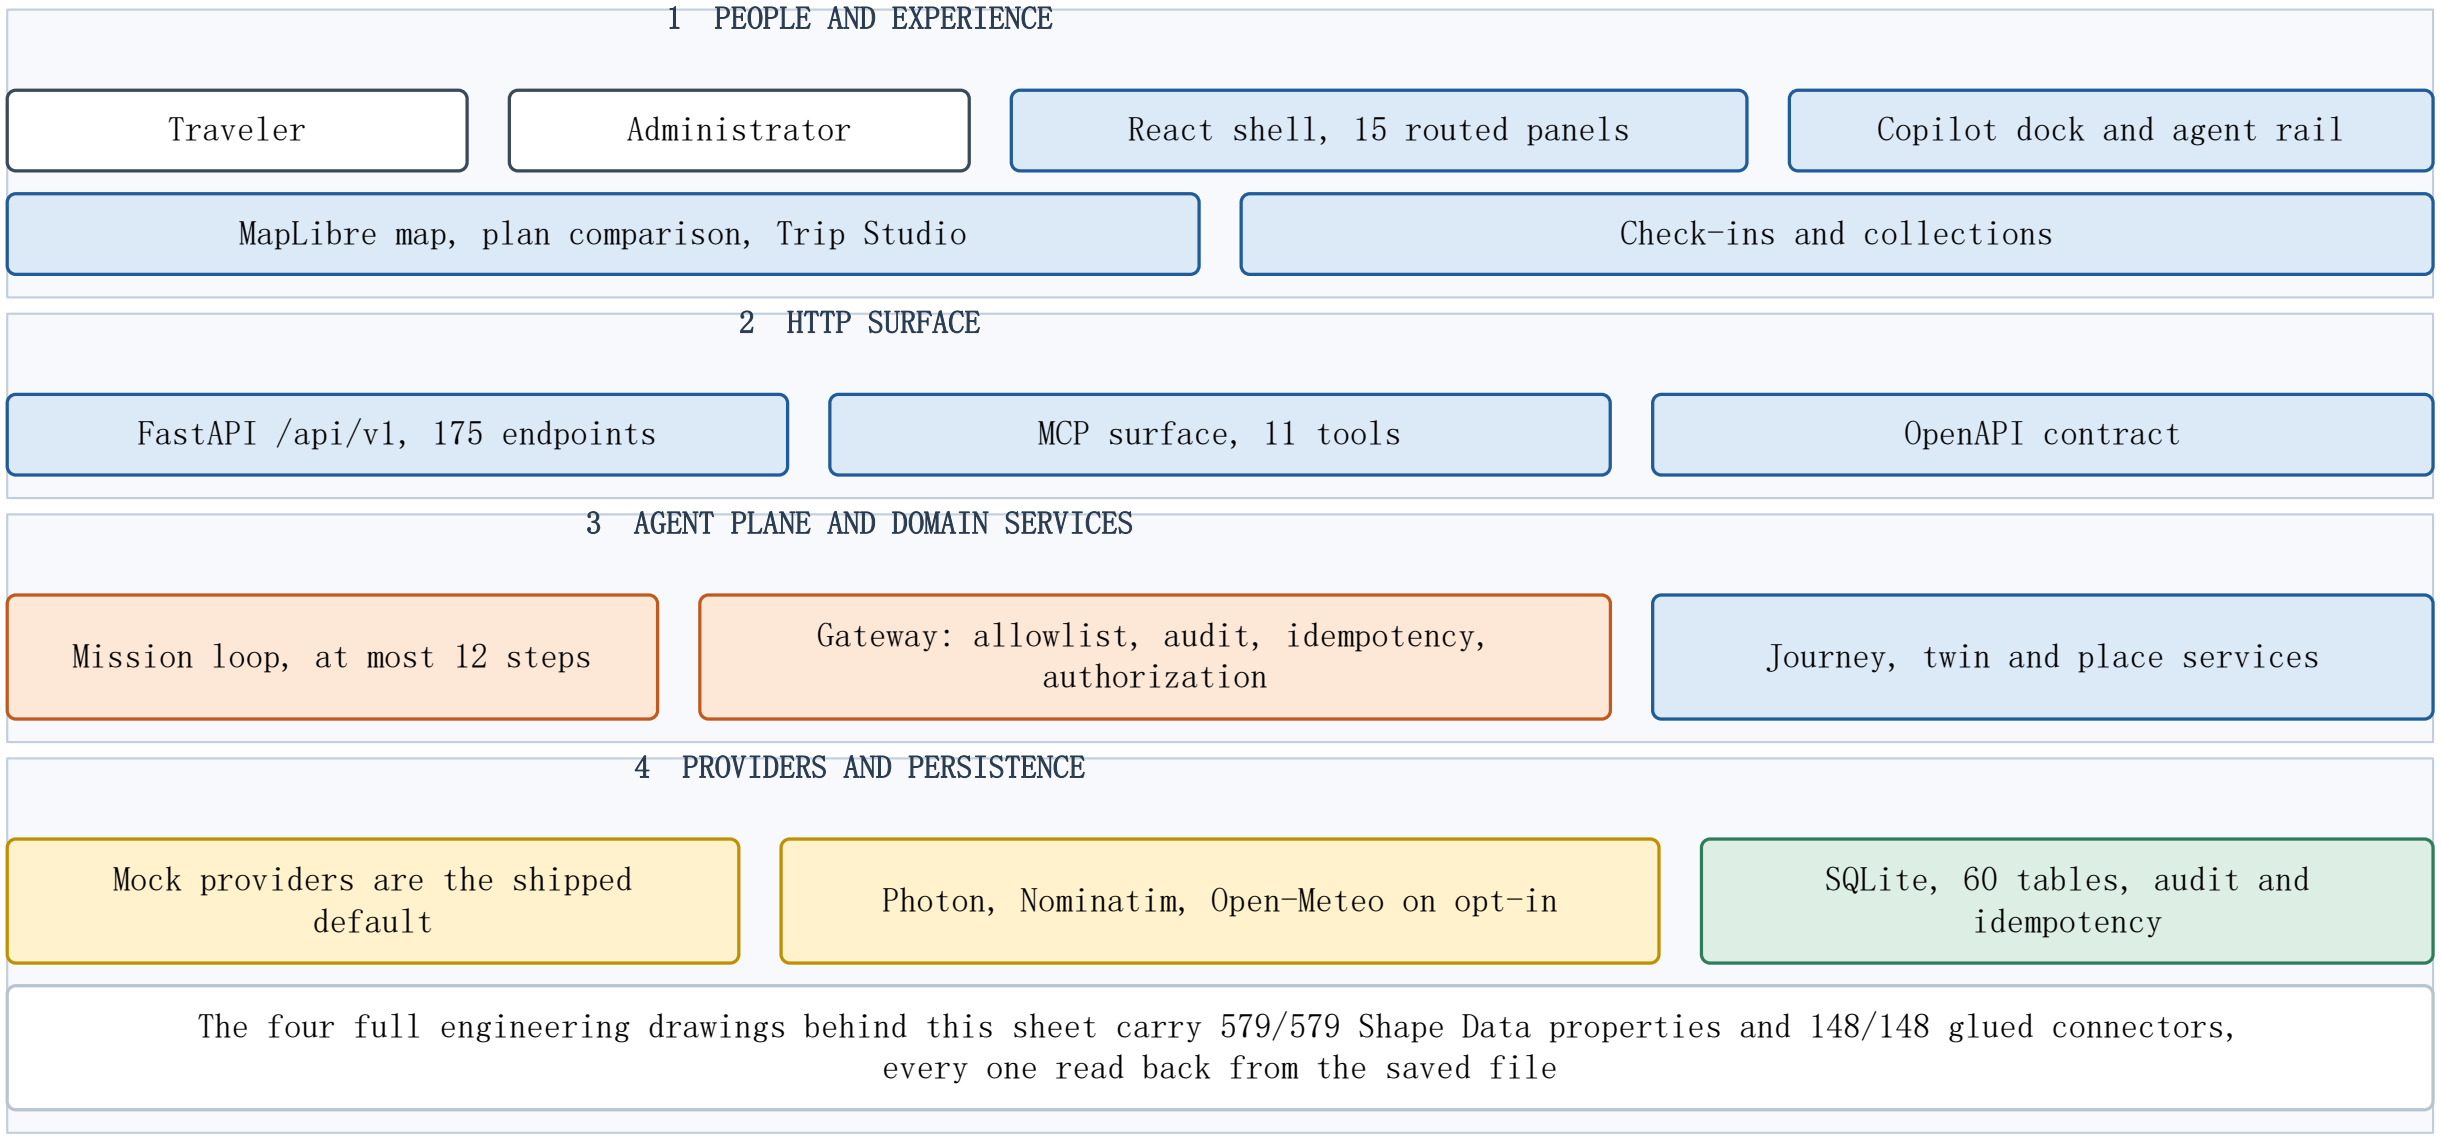

CityNexus | How the agent is bounded

CNX-SE-DECK-2 agent flow • plan sha256 4cd35d0725c2 • generated 2026-10-23 02:17
generated 2026-10-23 02:17

Drawn from gateway.py as measured on 2026-10-22: the order of the doors is the code's order, not a diagram convention.

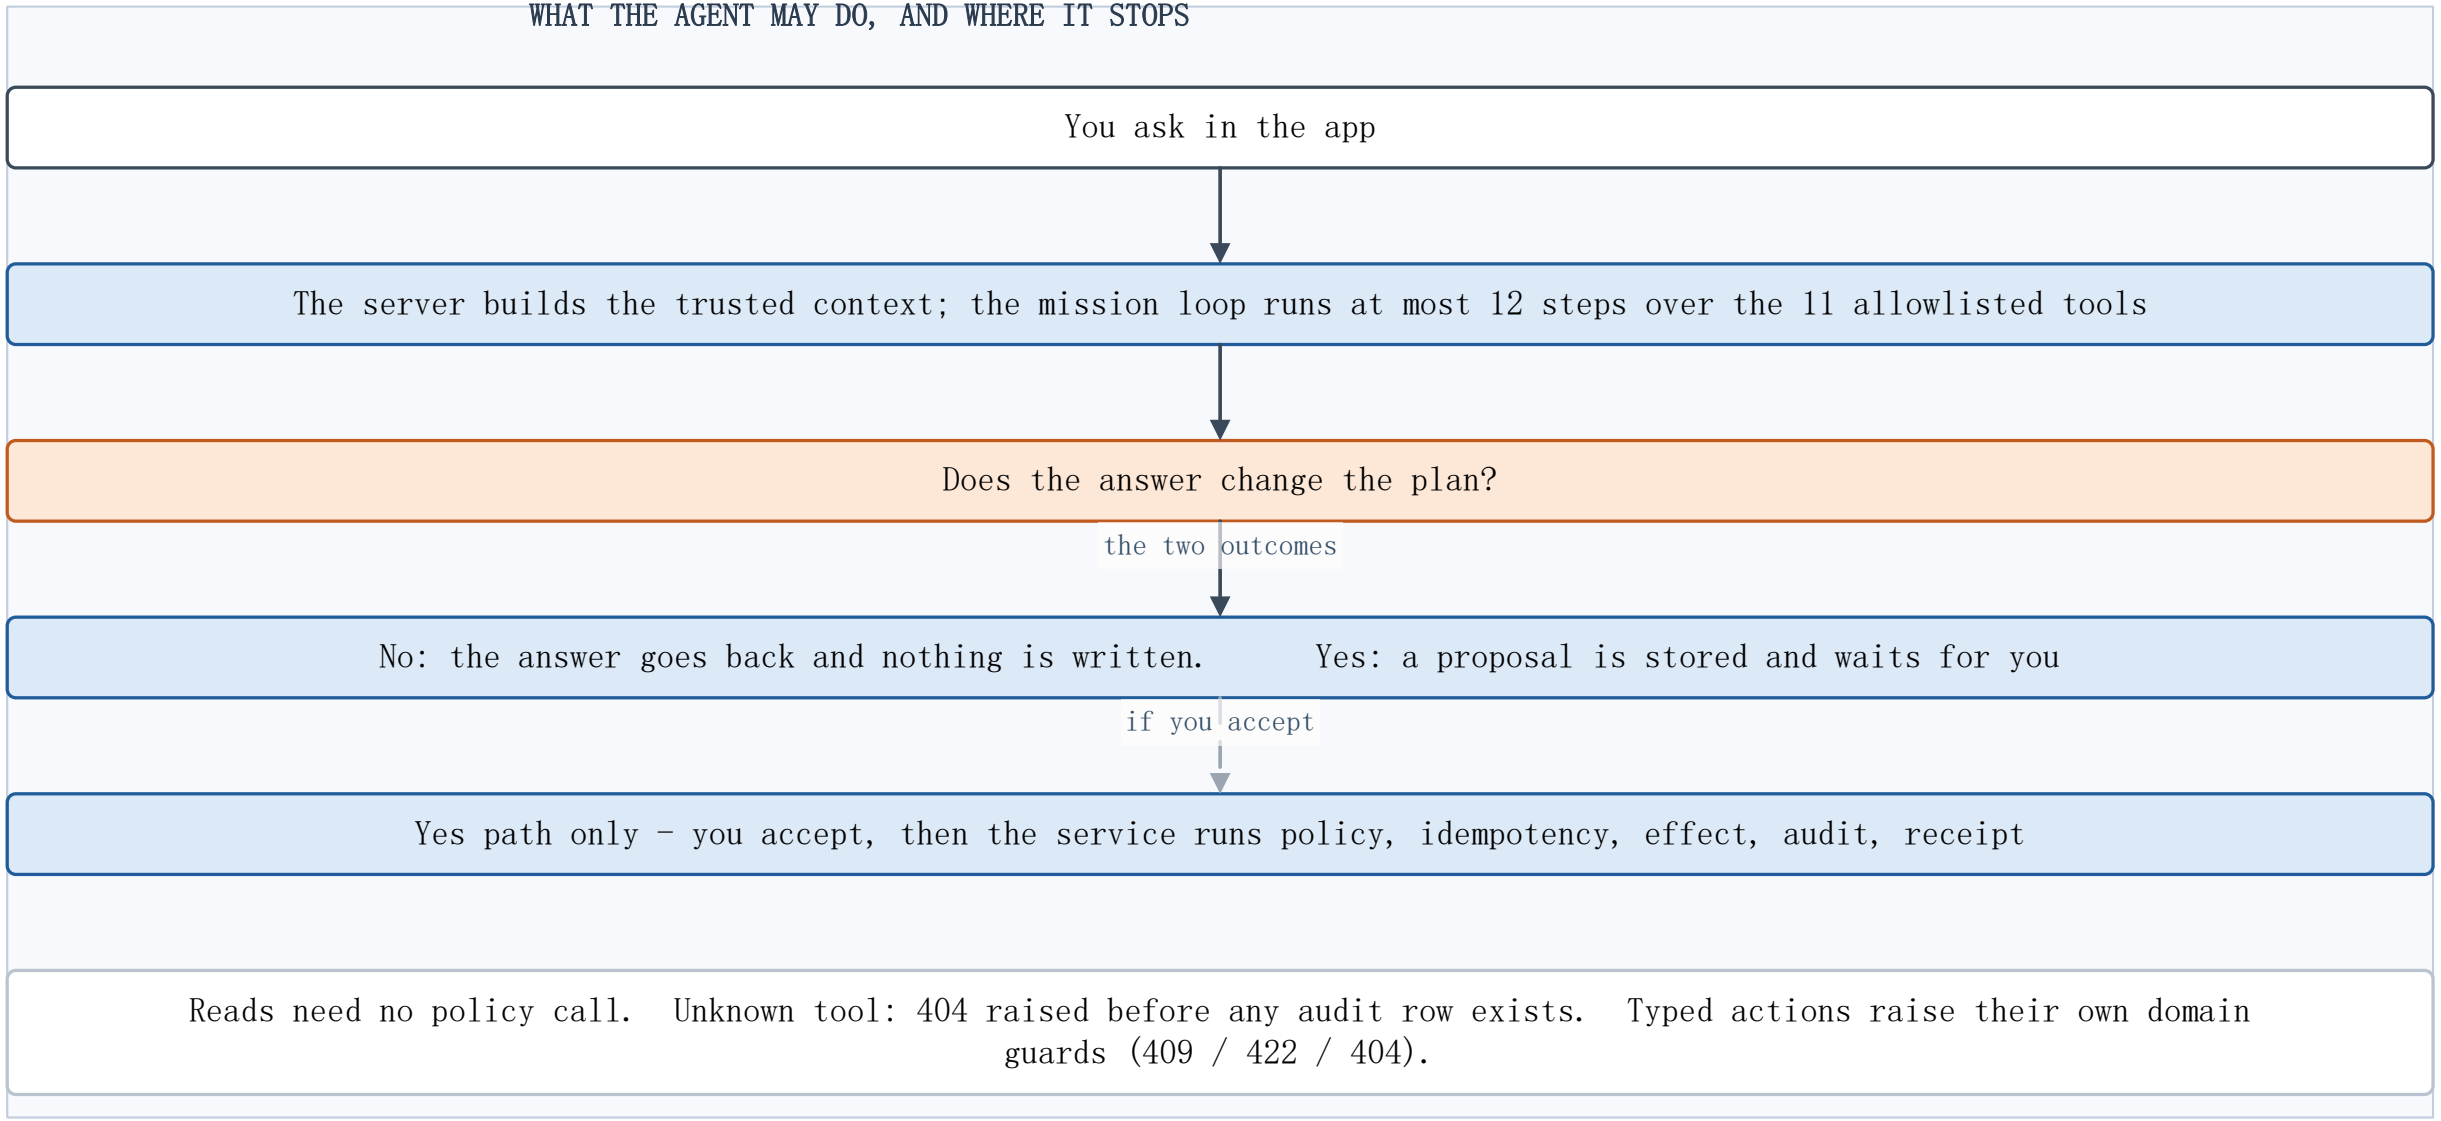

CityNexus | Progress, blockers and lateness

generated 2026-10-23 02:17

Every figure on this sheet is read out of the shipped .mpp by the build that produced it; nothing is typed. Part 1's course-platform submission is still not evidenced, so no row here claims it was made.

WHERE THE PLAN STANDS AT THE STATUS DATE 2026-10-22

the plan as built 65 rows, 41 tasks	dependencies 61 written, 0 violate	student effort 221 h, peak 19.9 of 20	cost and finish $4461, 2026-10-23
recovery forecast 2026-11-04, one day early	late rows 14 past plan, none finished	over-allocation 0 person-weeks (gate refuses >0)	

BLOCKERS, AND EIGHT OF THE 14 LATE ROWS (WBS, percent complete, forecast finish)

Valhalla live routing: no URL configured, the travel matrix stays mocked	Native Hermes binary absent; runtime identity is still DIRECT	No real payment or refund instrument registered
Impact resolver disabled by default in configuration	Phone and PWA shadow trial not performed	Requirement baseline not approved by the teacher as customer

2.5 0%, planned 10-21, forecast 10-27	5.2 70%, planned 09-18, forecast 10-23	5.3 0%, planned 09-21, forecast 10-28	6.5 20%, planned 10-07, forecast 10-29
8.2 50%, planned 09-23, forecast 10-27	9.1 85%, planned 10-21, forecast 10-27	9.2 60%, planned 10-21, forecast 11-03	9.3 50%, planned 09-30, forecast 10-27

CityNexus | Who does what, and what it costs

Three students at a declared availability, two compute lanes priced separately so machine work never looks like labour hours.

CNX-SE-DECK-4 resources • plan sha256 4cd35d0725c2 • generated 2026-10-23 02:17
generated 2026-10-23 02:17

STUDENT EFFORT AGAINST DECLARED AVAILABILITY

Yang Jianbin 0802240329 requirements, architecture, integration	78 h of 140 h available	peak week 19.9 h 0 week(s) over
Wang Jiarui 0802240322 data integration, scopes, testing	75 h of 140 h available	peak week 17.2 h 0 week(s) over
Wang Xinyue 0802240324 frontend, agent surface, SRS writing	68 h of 140 h available	peak week 19.6 h 0 week(s) over

Availability is an assumption for each member to confirm: 20 h per week while the module runs. Total student effort 221 h.

NOT STUDENT LABOUR

Qoder agent lanes material resource: priced, zero student hours	Codex co-development material resource: priced, zero student hours

7 priced compute assignments; 0 rows are staffed by a lane alone and still carry student hours.
The duty split is a plan proposal, not a confirmed record: git shows one commit identity for all three members.
