CityNexus | Software Engineering 2026 - plan on one page

CNX-SE-BRF-01 derived from CityNexus_Software_Engineering_Plan.mpp sha256 43030b3626b19b5e
generated 2026-10-22 18:30

A print view of the schedule Microsoft Project computed in CityNexus_Software_Engineering_Plan.mpp. Bars are the eleven phase rollups; the diamonds are the thirteen milestones; nothing here is a second plan, and no date on this page was typed by hand.

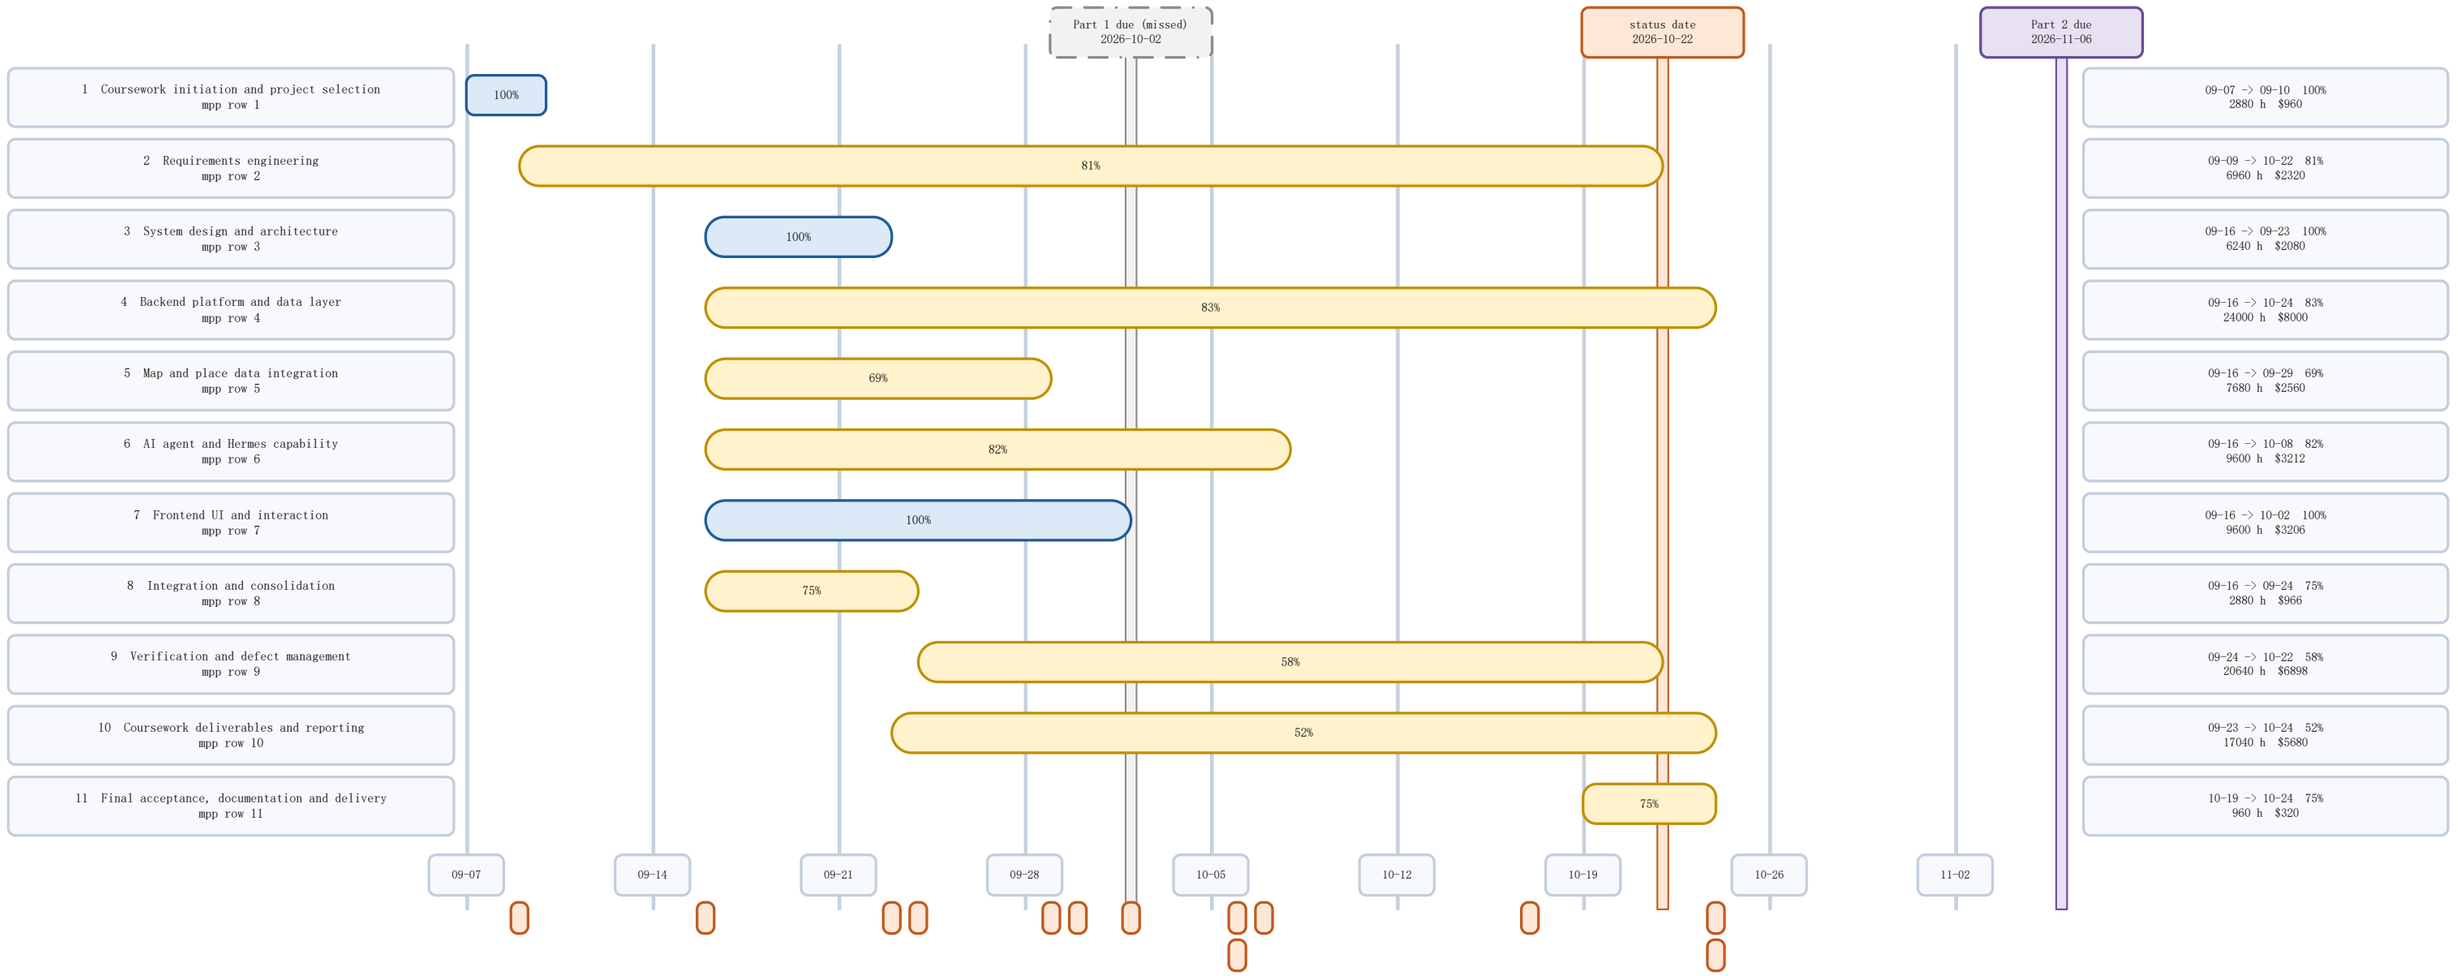

MILESTONES, in date order - the schedule's own computed dates

- M1 Topic and scope agreed 09-09
- M2 Requirements baseline drafted 09-16
- M3 Architecture design complete 09-23
- M8 Integration line stable 09-24
- M5 Provider mesh integrated behind on 09-29
- M10 Part 1 deadline (recorded as misse 09-30 dl 10-02
- M7 Frontend running against the real 10-02
- M4 Core backend running end to end 10-06
- M6 Agent surface proven against a liv 10-06
- M9 System test complete 10-07 dl 11-02
- M11 Mid-term review 10-17 dl 10-22
- M12 Part 2 submission deadline 10-24 dl 11-06
- M13 Final coursework delivery 10-24 dl 11-06

WHAT MICROSOFT PROJECT COMPUTED

- rows: 65 (11 groups, 41 tasks, 13 milestones)
- dependencies: 61 written, 0 violating date order
- constraints: 0 (every row is As Soon As Possible)
- labour hours: 1808 h
- cost: $36202
- critical rows: 4
- finish: 2026-10-24
- late at status date: 4 open rows

HOW TO READ: each row is one WBS group, drawn from its computed start to its computed finish on a Mon-Fri calendar anchored at 2026-09-07, the first working day on or after the repository's first commit. The right-hand figures are the group's own work hours and cost as Project derived them from duration x assignment units x 8 h/day.

MILESTONES ARE NOT SEQUENTIAL GATES. The repository shows backend, frontend, contracts and the integration line changing on the same days from 2026-09-19, so a later-numbered milestone can land on an earlier date; the numbering is WBS order, not calendar order.

THE THREE VERTICAL LINES: Part 1 was due 2026-10-02 and its row is still at 0%, which is why that line is drawn in the missed style; the status date is 2026-10-22, the day this pack was produced; Part 2 is due 2026-11-06 and the plan's own finish precedes it.

WHAT THIS PAGE CANNOT SHOW: rows that are late against the status date stay late. Project's Move to Status Date was measured to be inert through COM on this install (se_proj_probe_r10.log), so unfinished work was not silently pushed into the future to make the picture tidy. The full 65-row plan, its links, resources, costs and critical path are in the .mpp.

Legend

- phase complete at the status date
- phase in progress
- not started / date missed
- status date, milestones
