CityNexus | System at a glance

Four layers and one rule: the agent proposes, the domain services decide. Every box is a real component in the reviewed tree.

CNX-SE-DECK-1 architecture • plan sha256 6398e58f9b4c • generated 2026-10-23 04:37
generated 2026-10-23 04:37

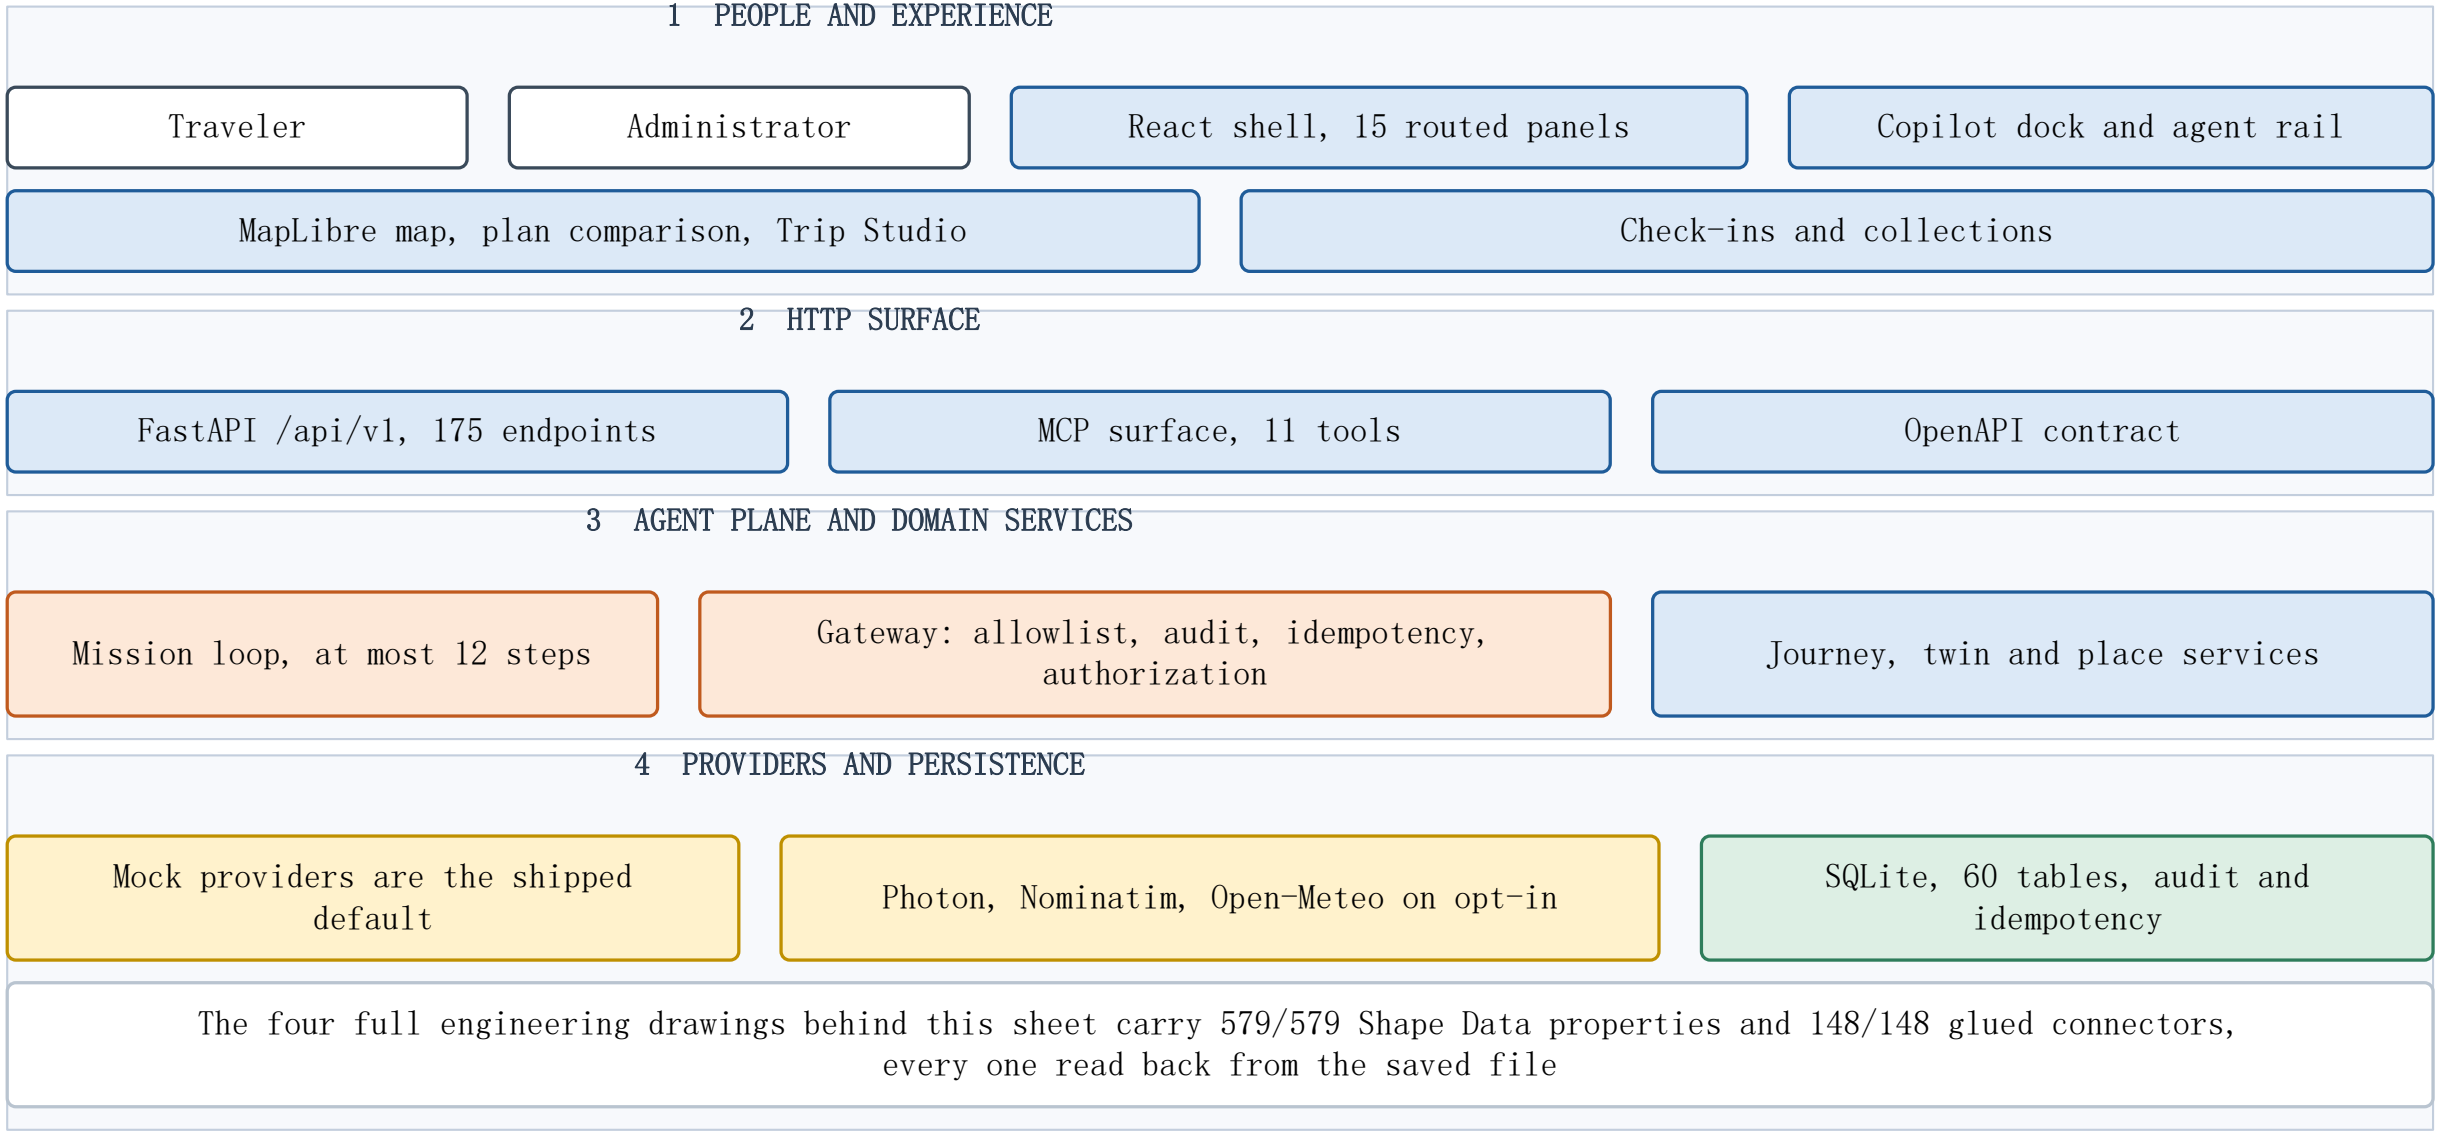

CityNexus | How the agent is bounded

CNX-SE-DECK-2 agent flow • plan sha256 6398e58f9b4c • generated 2026-10-23 04:37
generated 2026-10-23 04:37

Drawn from gateway.py as measured on 2026-10-22: the order of the doors is the code's order, not a diagram convention.

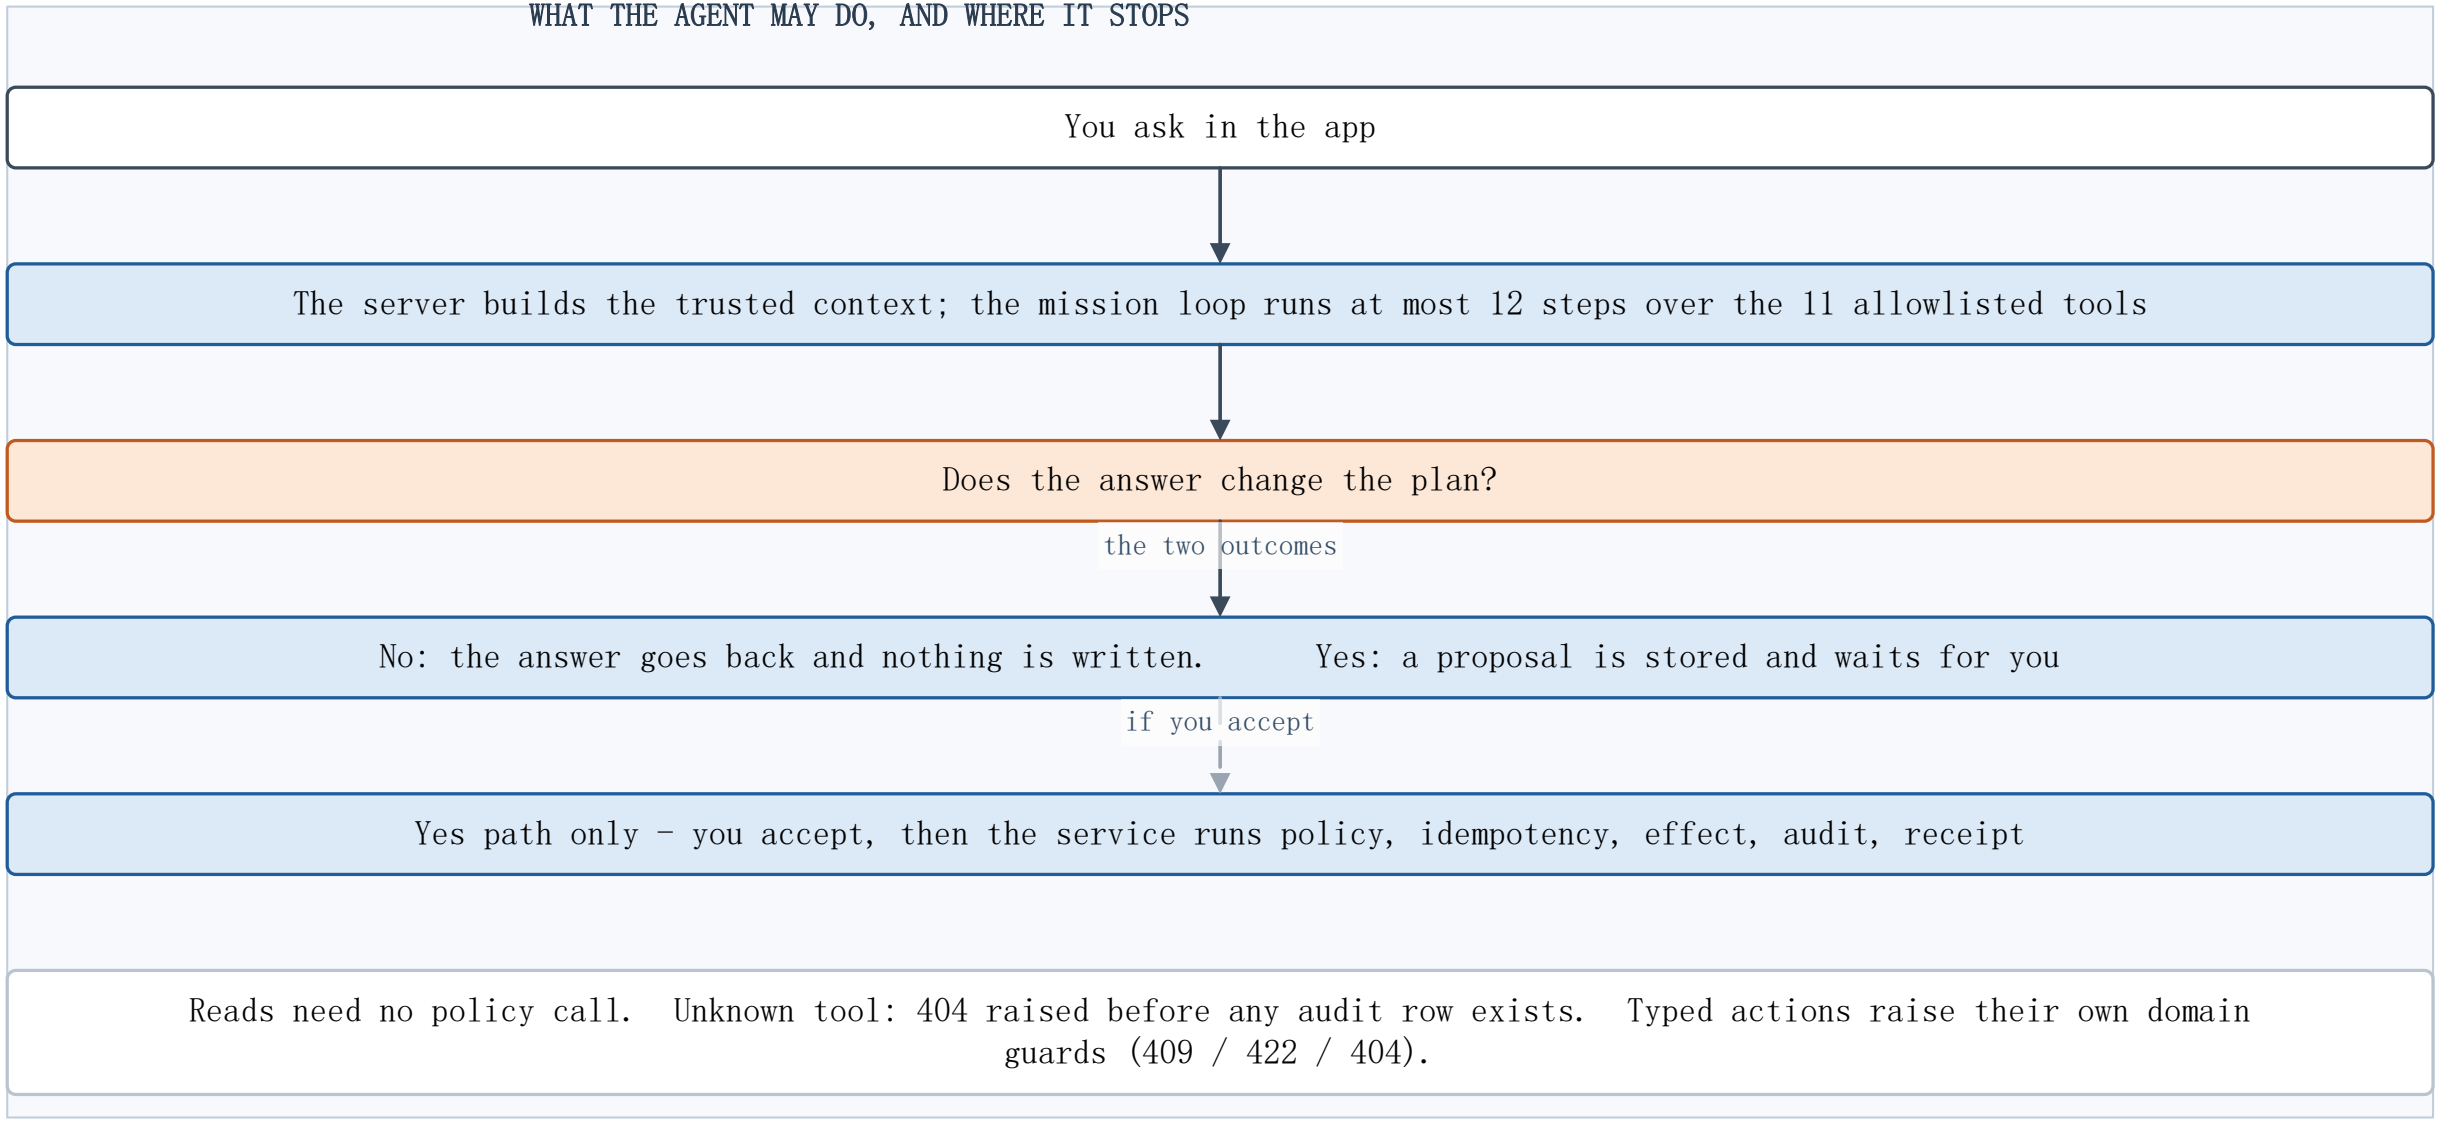

CityNexus | Progress, blockers and lateness

generated 2026-10-23 04:37

Every figure on this sheet is read out of the shipped .mpp by the build that produced it; nothing is typed. Part 1's course-platform submission is still not evidenced, so no row here claims it was made.

WHERE THE PLAN STANDS AT THE STATUS DATE 2026-10-22

- the plan as built — 65 rows, 41 tasks
- dependencies — 61 written, 0 violate
- student effort — 221 h, peak 19.9 of 20
- cost and finish — $4461, 2026-10-23
- recovery forecast — 2026-11-04, one day early
- late rows — 14 past plan, none finished
- over-allocation — 0 person-weeks (gate refuses >0)

BLOCKERS, AND EIGHT OF THE 14 LATE ROWS (WBS, percent complete, forecast finish)

- Valhalla live routing: no URL configured, the travel matrix stays mocked
- Native Hermes binary absent; runtime identity is still DIRECT
- No real payment or refund instrument registered
- Impact resolver disabled by default in configuration
- Phone and PWA shadow trial not performed
- Requirement baseline not approved by the teacher as customer
- 2.5 0%, planned 10-21, forecast 10-27
- 5.2 70%, planned 09-18, forecast 10-23
- 5.3 0%, planned 09-21, forecast 10-28
- 6.5 20%, planned 10-07, forecast 10-29
- 8.2 50%, planned 09-23, forecast 10-27
- 9.1 85%, planned 10-21, forecast 10-27
- 9.2 60%, planned 10-21, forecast 11-03
- 9.3 50%, planned 09-30, forecast 10-27

CityNexus | Who does what, and what it costs

Three students at a declared availability, two compute lanes priced separately so machine work never looks like labour hours.

CNX-SE-DECK-4 resources • plan sha256 6398e58f9b4c • generated 2026-10-23 04:37
generated 2026-10-23 04:37

STUDENT EFFORT AGAINST DECLARED AVAILABILITY

Yang Jianbin 0802240329 requirements, architecture, integration	78 h of 140 h available	peak week 19.9 h 0 week(s) over
Wang Jiarui 0802240322 data integration, scopes, testing	75 h of 140 h available	peak week 17.2 h 0 week(s) over
Wang Xinyue 0802240324 frontend, agent surface, SRS writing	68 h of 140 h available	peak week 19.6 h 0 week(s) over

Availability is an assumption for each member to confirm: 20 h per week while the module runs. Total student effort 221 h.

NOT STUDENT LABOUR

Qoder agent lanes material resource: priced, zero student hours	Codex co-development material resource: priced, zero student hours

7 priced compute assignments; 0 rows are staffed by a lane alone and still carry student hours.
The duty split is a plan proposal, not a confirmed record: git shows one commit identity for all three members.
